



City of Chico

SR32 Widening Project (Phase 2)

Volume 7

October 21, 2016

State Route 32 Widening Project (Phase 2) Update

Introduction

Following is the construction update newsletter for the SR32 Widening Project (Phase 2). The purpose of these updates is to share detailed information regarding schedule and construction activities anticipated for the upcoming week(s). If you do not wish to receive updates, you may opt out by sending staff a quick e-mail with that instruction. Alternatively, if you know of other interested parties that would appreciate being added to the list, please send an email request to: update32@chicoca.gov

Southbound Fir Street Closure - The southbound lane of Fir Street between east and west bound SR32 has been closed to south bound traffic. No south bound traffic will be allowed. This is a permanent traffic pattern change. Fir Street is open for north bound traffic only. Please pay attention to construction area signs and delineation at all times. Motorists are encouraged to seek alternate routes and allow adequate time in their schedule. Access to Fir Street/Humboldt Avenue can be made from Forest Avenue or by southbound SR99/SR32 Couplet to eastbound SR32 to Fir Street (SEE ATTACHED GRAPHIC).

Anticipated Night Work, Weekend Day Work and Lane Closures for Grinding and Paving

Tonight and this weekend, the Contractor will be working a combination of day and night shifts. The Contractor will be performing night work **Friday night (10/21) through Saturday morning (10/22)** to do pavement grinding. **Saturday (10/22) and Sunday (10/23)** the Contractor will be performing **day work** to do asphalt paving. These operations will have heavy equipment running throughout Friday night/Saturday morning and throughout the day on Saturday and Sunday. Night work hours will generally be from 7pm to 7am. Day work hours will generally be from 6am to 5pm. Lane closures will be implemented to perform the work. Delays can be expected. It is our continued intention to minimize night work whenever possible but it is necessary for safety and to minimize impacts to the heavy daytime commuter and school traffic. This schedule is also necessary to complete the work in advance of rain expected late Sunday through Tuesday.

Traffic Signals, Concrete, Signage and Traffic Shifts

Throughout next week, the Contractor continues installation of traffic signalization, placement of aggregate base/concrete, and installation of traffic signs. Minor traffic shifts should be expected.

CONTINUED ON NEXT PAGE

Minor traffic delays should be expected. Access to all residences and businesses within the construction zone will be maintained throughout the duration of the project. Please be sure to travel through the area with caution, paying attention to revised traffic alignments, signing and devices. Other safety tips include:


- ✓ Drive slowly and carefully through the construction area.
- ✓ Be alert for construction workers and large equipment, such as backhoes, graders and trucks.
- ✓ Obey all construction signs and directions from traffic control flaggers.

The City appreciates your patience and understanding during the project. Please feel free to contact City staff or the Contractor should you need additional information. The Contractor will notify residents & businesses prior to the commencement of any construction activities that may affect or is in the immediate vicinity of their property. For more information, please refer to the City Capital Project Services website at www.ci.chico.ca.us Pull down the Departments drop down menu and select Capital Project Services. The same web page can be accessed at the following link:

www.ci.chico.ca.us/capital_project_services/home_page.asp


CONTACT PHONE NUMBERS (Area Code – 530)	
Capital Project Services Department	879-6900
Police Dispatch (use this number for immediate assistance from 5PM - 8AM)	895-4911
<u>Design Questions</u>	
Craig Murray, Civil Engineer	879-6931
<u>Construction Issues</u>	
Keith Flaherty, Resident Engineer	(916)-826-3943
Ande Stevens, Construction Inspector	(775)-686-9590
<u>Knife River Construction (Contractor)</u>	
Marc Madsen (Project Manager)	218-2302
24-hour Contractor contact	891-6555

Area of Construction Activities (June 2016-January 2017)

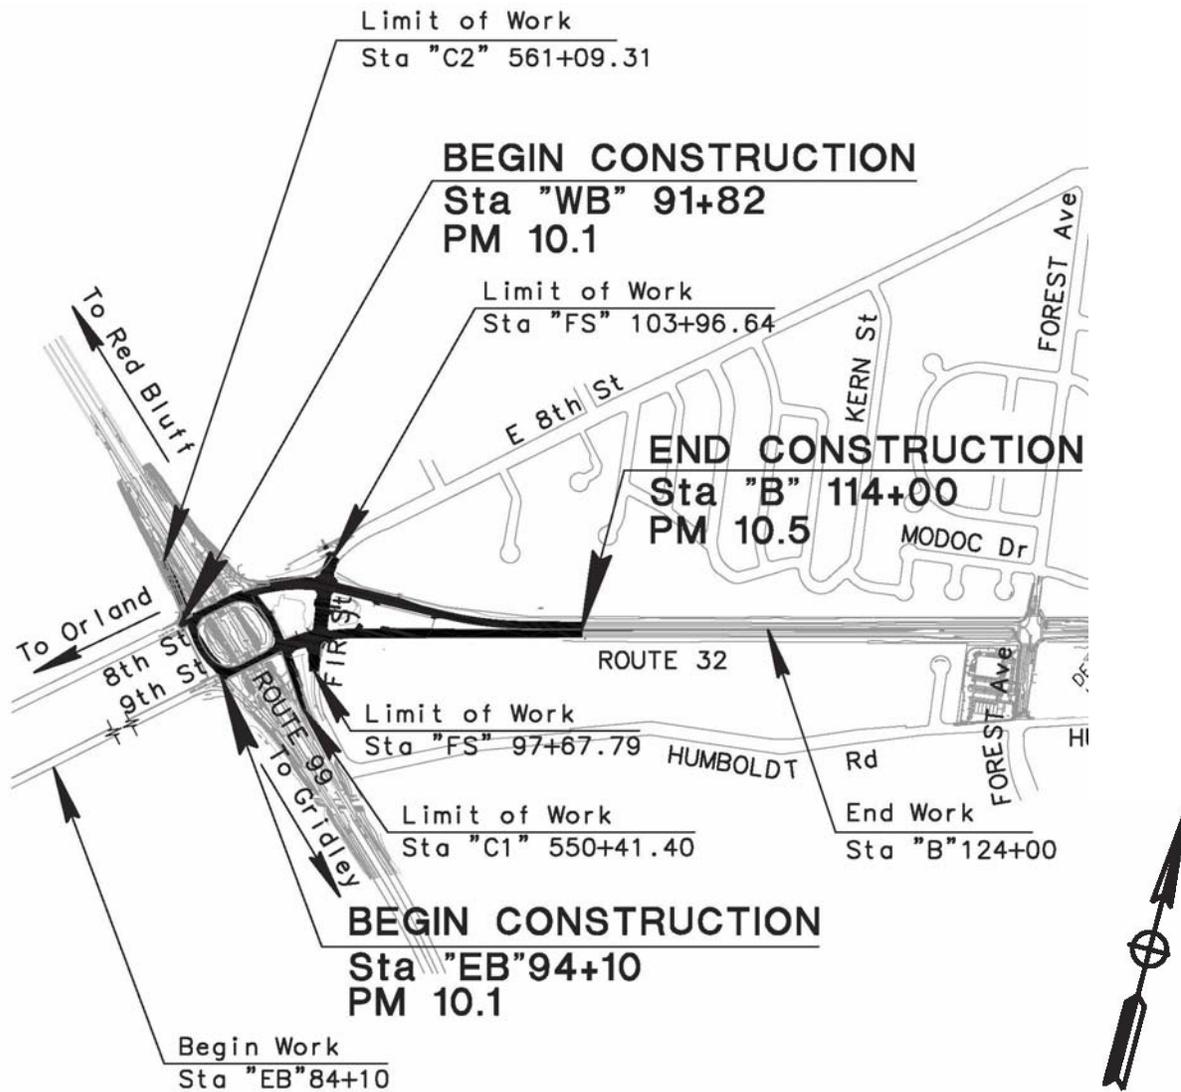

CONTINUED ON NEXT PAGE

Lane Closure – Southbound Fir Street between eastbound and westbound SR32

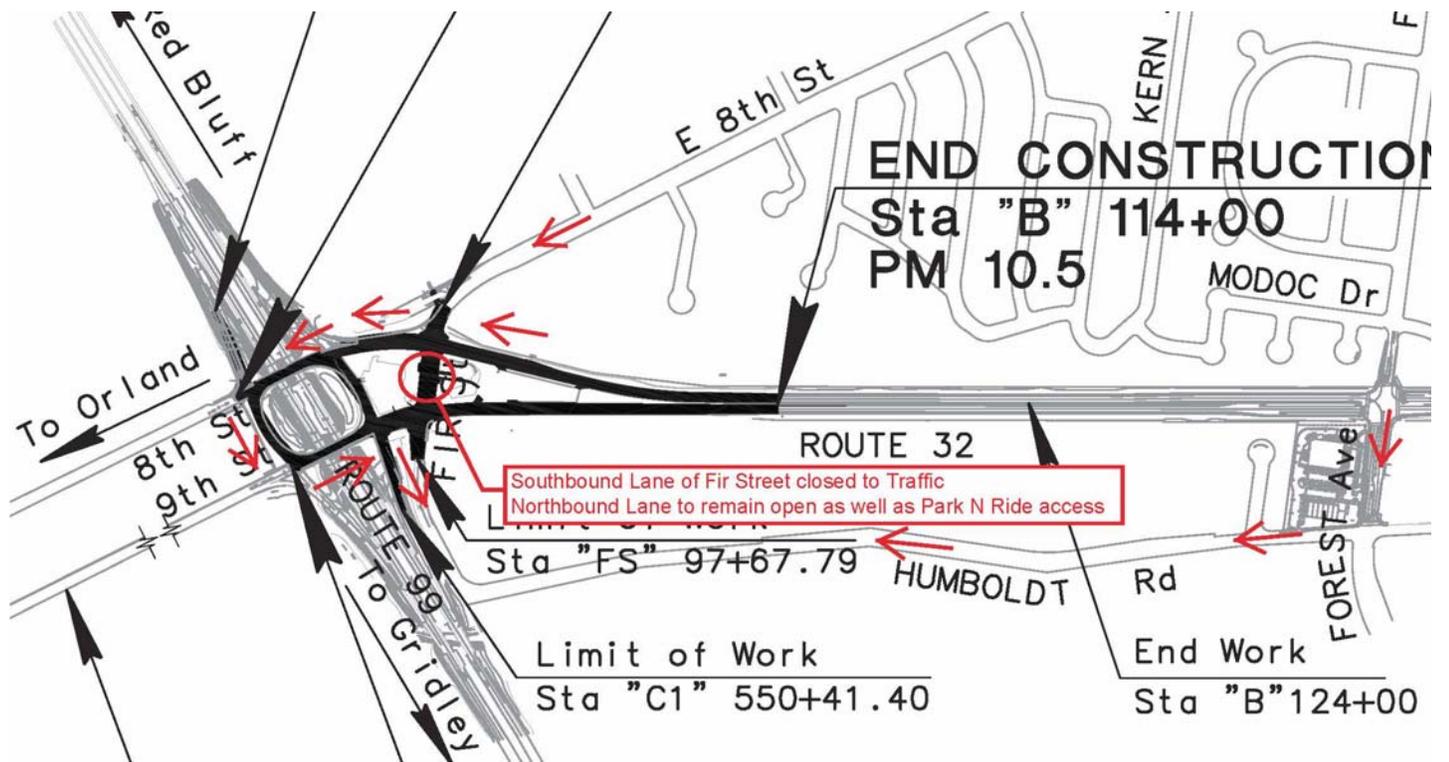

END
